ID	Task Name	Duration	Start	Finish
1	**Water Main Replacement Project**	**238 days**	**Wed 3/20/13**	**Fri 2/14/14**
2	**Notice To Proceed**	**1 day**	**Wed 3/20/13**	**Wed 3/20/13**
3	**Complete Field Survey**	**17 days**	**Tue 4/23/13**	**Wed 5/15/13**
4	**NEPA Approval**	**47 days**	**Mon 4/15/13**	**Tue 6/18/13**
5	**Water Main Design Engineering**	**134 days**	**Wed 3/20/13**	**Mon 9/23/13**
6	Provide Preliminary Alignment	1 day	Mon 4/29/13	Mon 4/29/13
7	50% Design	83 days	Wed 3/20/13	Fri 7/12/13
8	50% QA/QC	1 day	Wed 7/10/13	Wed 7/10/13
9	50% Client Review	10 days	Mon 7/15/13	Fri 7/26/13
10	90% Design	35 days	Mon 7/15/13	Fri 8/30/13
11	90% QA/QC	1 day	Wed 8/28/13	Wed 8/28/13
12	90% Client Review	15 days	Mon 9/2/13	Fri 9/20/13
13	Final Design	16 days	Mon 9/2/13	Mon 9/23/13
14	Permits	105 days	Mon 4/8/13	Fri 8/30/13
15	**Bid and Award**	**30 days**	**Mon 9/23/13**	**Fri 11/1/13**
16	Bid Process	17 days	Mon 9/23/13	Tue 10/15/13
17	Award and Contracts	13 days	Wed 10/16/13	Fri 11/1/13
18	**Construction**	**75 days**	**Mon 11/4/13**	**Fri 2/14/14**
19	"U" Street Water Main	25 days	Mon 11/4/13	Fri 12/6/13
20	"Z" Street Water Main	25 days	Mon 12/9/13	Fri 1/10/14
21	Birch Street Water Main	25 days	Mon 1/13/14	Fri 2/14/14

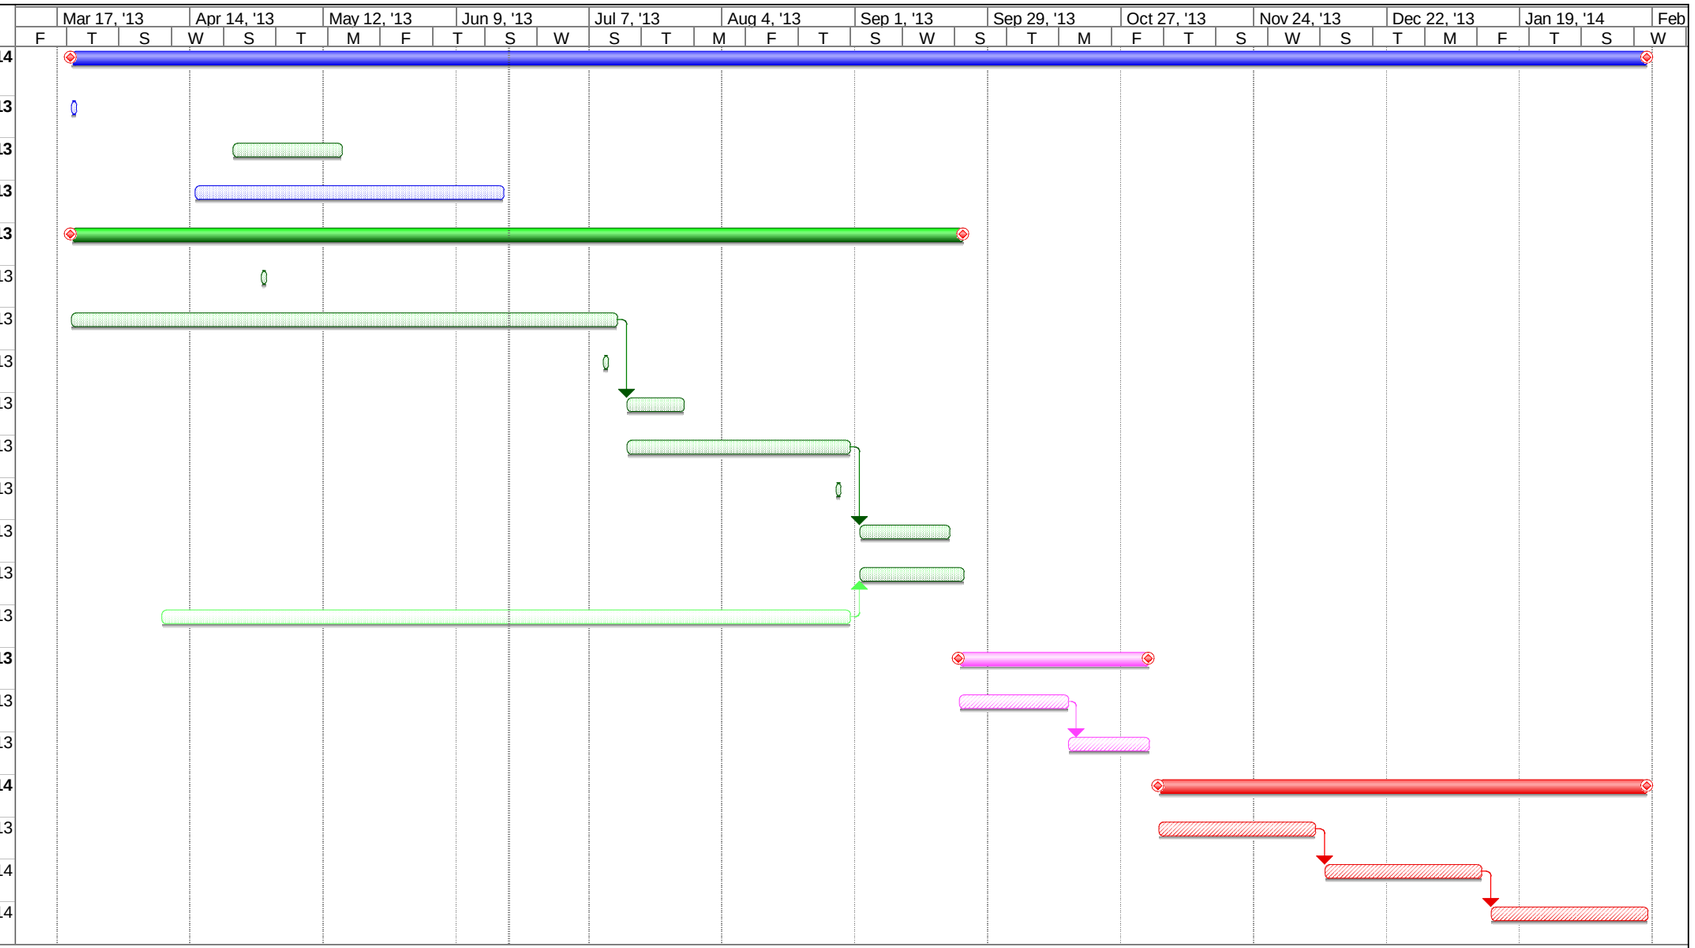

Project: Schedule
Date: Thu 6/20/13

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
